

Himachal Pradesh Rural Water Supply Project (NDB Funded)




- Project Approved by DEA on 29th November 2016.
- Project approved by BOD of NDB on 12th December 2021.
- Loan agreement signed by NDB on 22nd December 2022.
- Loan effectiveness date 25th January 2022
- Project completion date: August 2025
- Expenditure incurred: 108.95Cr. (Including SOP)
- Reimbursement claim filed: 60.92Cr. (Excluding SOP)

Project Cost: \$100 million (743 Cr.)
NDB share: \$80 million (594.4 Cr)
GoHP share: \$20 million (148.6 Cr)

No. of Schemes	24	No. of Packages	18
-----------------------	----	------------------------	----

Water facility to the left out / partially covered habitations in rural areas state of Himachal Pradesh

	Population	4,62,194
	FHTC (@ 70 LPCD)	45,498 (2018)
	Habitations	3154
	Villages	1255
	Districts Involved	8

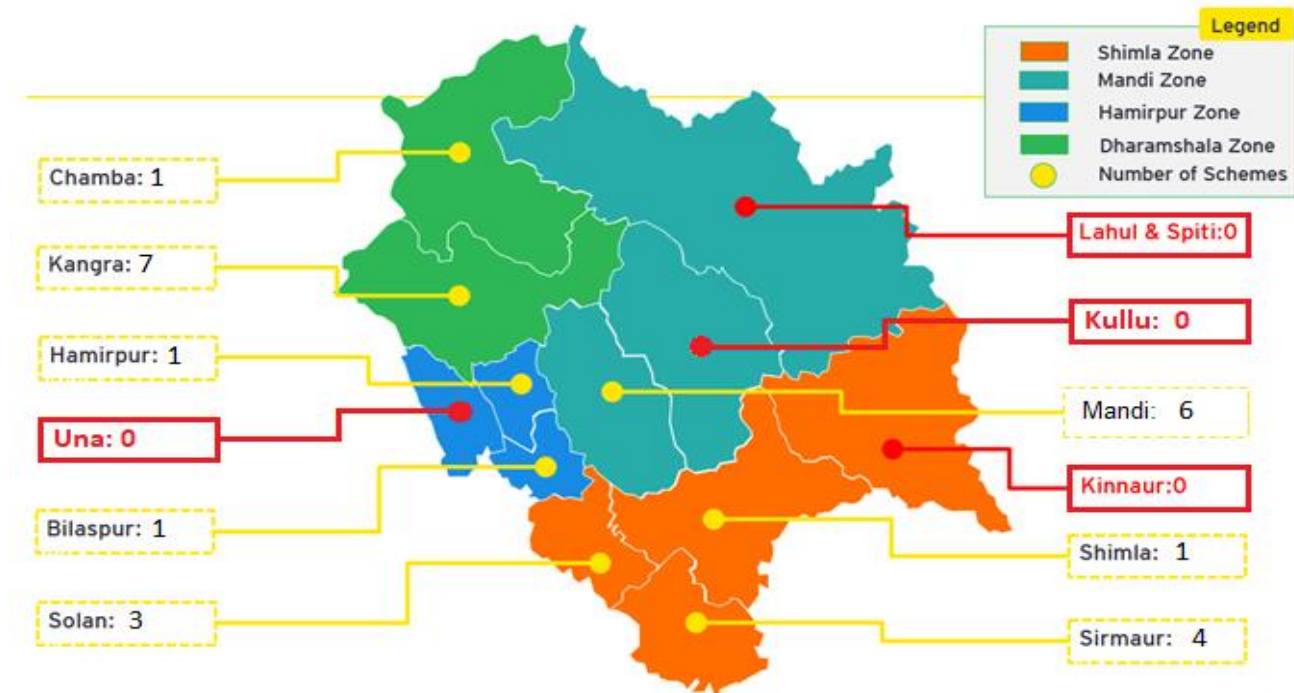

Detail of Awarded Works (Work In Progress)

Sr.	Package No.	District	Consty.	Population	Name of scheme	A/A Amount (inCr.)	Awarded Amount i/c 5year O&M (InCr.)	Upto date Expdt. (InCr.)	Physical Progress (%)
1	D-2	Kangra	Jawali	25306	Providing drinking water facilities for Ghar Jarot & Multi villages piped water supply scheme for Part of Nagrota Suriyan Block of Kangra District (H.P)	29.65	28.25	2.90	10%
2	D-3	Kangra	Sullah	16378	Providing drinking water facilities for Parour Khas & Multi villages group piped water supply scheme for Part of Bhawarna & Bhedu Mahadev Block (Sullah) of Kangra District. Providing drinking water facilities for Gharoon (Malnoo) & Multi villages group piped water supply scheme for Part of Bhawarna & Bhedu Mahadev Block (Sullah) of Kangra Distt.	31.68	33.81	7.65	18%
3	D-6	Kangra	Nagrota	18123	Providing drinking water facilities for Massal and Multi Villages group piped water supply scheme for the part of Nagrota Bagwan Block in Tehsil Nagrota Bagwan Distt Kangra HP	21.01	25.61	4.52	25%
4	D-5	Kangra	Indora	9215	LWSS to Village Makroli Chatter ,Behri Dhiala,Gadhrana & Dini in Tehsil Indora Distt. Kangra (HP)	27.72	33.07	9.38	30%
5	D-7	Kangra	Dehra	31760	LWSS to PC Habitations of village Haripur Multi Village Piped Water Supply Scheme for Nagrota Surian Block of Tehsil Dehra Distt. Kangra (HP)	59.48	61.38	13.35	35%
6	S-1	Shimla	Jubbal Kothkhai	20461	LWSS to PC habitation under Jubbal Kothkhai Block from Pabbar River in District Shimla	38.07	44.52	8.16	15%
7	M-1	Mandi	Balh	15515	LWSS to PC habitations under I&PH Sub Division Rewalsar, Tehsil Balh, District, Mandi (HP)	43.90	45.69	9.92	25%

Sr.	Package No.	District	Consty.	Population	Name of scheme	A/A Amount (InCr.)	Awarded Amount i/c 5year O&M (InCr.)	Upto date Expdt. (InCr.)	Physical Progress (%)
8	M-2	Mandi	Drang	38607	LWSS to PC habitation in GP Baridhar, Kufri, Silag, Badhwahan, Kunnu, Palli, Suin, Dalah, Gwali and Tandoo	60.57	81.06	16.42	25%
					LWSS to PC habitation in GP Sudhar, Tarswan, Shilbhadani, Zilan & Urla				
					WSS to PC habitation in GP Dhamchain, Bardwahan, Lapas & Latrain				
9	S-2	Nahan	Nahan	8722	LWSS Devka Purla and other multi villages for part of block Nahan tehsil Nahan Distt. Sirmour HP	17.85	25.34	4.33	10%
10	S-3	Sirmour	Pachchhad	16598	Providing LWSS to various Villages in GP Narag Nohr, Dilman, Naina Tikker, Saria, Mahlog, Lal Tikker, dradli, sadhnaghat, Daron Deoria, Sarol Chamanji and Wasni from Giri River in tehsil Pachchhad Distt. Sirmour (HP)	26.50	29.40	1.42	3%
11	D-1	Chamba	Dalhousie/ Bhattiyat	28514	Providing lift water supply scheme to various WSS under GP Bagho, Dhalog, Mornu, Sudli, Chuhan, Padhrotu, Manola, Rulyani, Osal, Bathri, Tappar, Nanai Khad, Velly, Balera, Jiunta, Tunnuhatti, Mail, Mornu, Samleo etc Dalhousie and Bhattiyat Distt. Chamba H.P	60.78	70.16	7.65	5%
12	H-2	Bilaspur	Naina Devi Ji	37626	Aug. of various water supply schemes under IPH Sub Division Swarghat in Tehsil Shri Naina Devi Ji Distt. Bilaspur	66.68	71.45	9.46	3%
13	D-4	Kangra	Nurpur	14126	Augmentation of various LWSS in Drought Hit Area of Nurpur Constituency in Tehsil Nurpur - Detailed Project Report for Nagini source villages group piped water supply scheme for Part of Nurpur Block of Kangra.	13.13	19.63	0.14	0

Sr.	Package No.	District	Consty.	Name of Division	Name of scheme	A/A Amount (InCr.)	Awarded Amount i/c 5year O&M (InCr.)	Upto date Expdt. (InCr.)	Physical Progress (%)
14	S-4	Sirmour	Shilai	53647	C/O WSS to 7 No.s Panchayats (Kamroo, Barwas,Shillai,Loza Manal Nainidhar, Sankholi and Tatyana) under Jal Shakti Division Shillai Distt. Sirmour	30.58	66.22	3.05	0
			Ponta		Aug.& improvement of WSS for group of Trans-Giri Panchyats in Tehsil Pounta Shahib Distt. Sirmour H.P	27.30			
15	M-4	Mandi	Sundernagar	11501	Multi village water supply scheme for 15 No Gram Panchyat of Jarol Kangoo aera under The Sunder Nagar Distt Mandi	31.79	37.75	0.62	0
16	M-3	Mandi	Nachan	11324	Multi village water supply Scheme for 9 No. Gram Panchayat of chailchowk area under chachyot in Distt Mandi.	30.74	36.86	1.50	0
			Total	357423		617.53	710.27	101.43	

TENDERS CALLED/UNDER PROCESS

Sr. No.	Package No.	District	Consty.	Population	Name of scheme	A/A Amount (inCr.	Upto date Expdt. (InCr. i/c SOP	Remarks
17	H-1	Barsar	Barsar	84446	Aug of source of various LWSS from River Beas of Barsar area (Barsar constituency) in Teh Barsar Distt Hamirpur.	137.57	5.94	Work yet to be awarded.
18	S-5	Solan	Arki	20325	Construction of LWSS to score, adjoining villages in GP Barel & Kandhar and other left out villages of Arki.	17.29	1.58	Tender to be recalled
			Solan		Aug. of LWSS Kothi Bara, LWSS Dharol Basha, GWSS Chhaush & GWSS Ganorari.	8.70		
			Nalagarh		Remodeling and renovation of old LWSS Nand, LWSS Rajwan Randhala, GWSS Doli & GWSS Jangli & adjoining villagrs in Tehsil Nalagarh.	19.68		
			Total	104771		183.25	7.52	
			G. Total	462194	G. TOTAL:-	800.79	108.95	

STATUS OF PROJECT

<p>Original Proposal</p>	<p>In original proposal there were 22 schemes in 16 packages. Tendering of 8 packages was done. Tender of 6 packages were cancelled due to high quoted rates and LOI for 2 works were issued and later on due to delay in approval of loan LOI issued was also cancelled.</p>
<p>Revised Proposal</p>	<p>Due to abnormal delay in approval from NDB, 9 schemes out of 22 prioritized schemes were got approved under other heads and now the project has been formulated for 24 schemes (18 packages) including 13 old schemes and 11 new schemes.</p>
<p>Project Details</p>	<ul style="list-style-type: none"> • Loan No. :- 21IN02 • Date of Project approval by Board of Director of NDB 8th December 2021. • Date of signing of Loan agreement by NDB 22nd December 2021. • Effective Date of loan 25th January 2022 • Closing date of loan 22nd August 2025
<p>Current Status of schemes</p>	<ul style="list-style-type: none"> • Out of 18 packages (24 schemes) tender for 16 packages (20 schemes) costing to ₹710.27 Cr have been awarded. And 2 packages (4 schemes) yet to be awarded. • ES studies completed and submitted. • PMC working.
